

ONEALPHA

Rebuild the operating core

CRM + Audit Platform + supporting modules

Ever Gauzy as an architecture reference

Management proposal | 13 September 2026

Decision focus: approve the discovery and foundation phase



Rebuild OneAlpha around one trusted business flow

A stronger platform foundation should make CRM and Audit work together without diluting CBQA-specific controls.

TODAY

- CRM and Audit enhancements evolve in parallel
- Generic platform concerns repeat across modules
- Workflow rules can drift between FE and BE
- Migration and UAT effort stays expensive



TARGET

- CRM becomes the upstream source for audit work
- Backend owns workflow state and permissions
- Shared platform services reduce duplication
- Agent-harness delivers in governed increments

Outcome: faster change with better traceability, control, and reuse

Gauzy proves the generic platform layer is buildable

Its value is in the patterns and the operating model, not in copying its domain implementation.

● ERP / CRM

Commercial records, proposals, contacts, billing

● HR / ATS

People, onboarding, qualifications, hiring

● Projects / Time

Projects, tasks, time, productivity

● Platform

Tenancy, APIs, plugins, dashboards, MCP

Reference lens: adopt the platform mechanics, adapt the business semantics, reject anything that conflicts with CBQA policy.

Three paths. One is the most balanced.

The choice should optimize business fit, delivery risk, and long-term ownership.

A Copy Gauzy

Fast generic start

Business fit

LOW

Delivery risk

HIGH

Low CBQA fit

High refactor + license risk

B Keep current only

Lowest transition risk

Business fit

HIGH

Delivery risk

MED

Slower platform improvement

Repeated cross-cutting work

C Reference + rebuild

Domain fit stays high

Business fit

HIGH

Delivery risk

MED


Foundation gets stronger

Requires disciplined phases

Suggestion: approve Path C and make discovery the first funding gate

OneAlpha becomes a modular platform with CBQA domain ownership

The architecture keeps generic platform services reusable while the Audit Platform owns its rules.

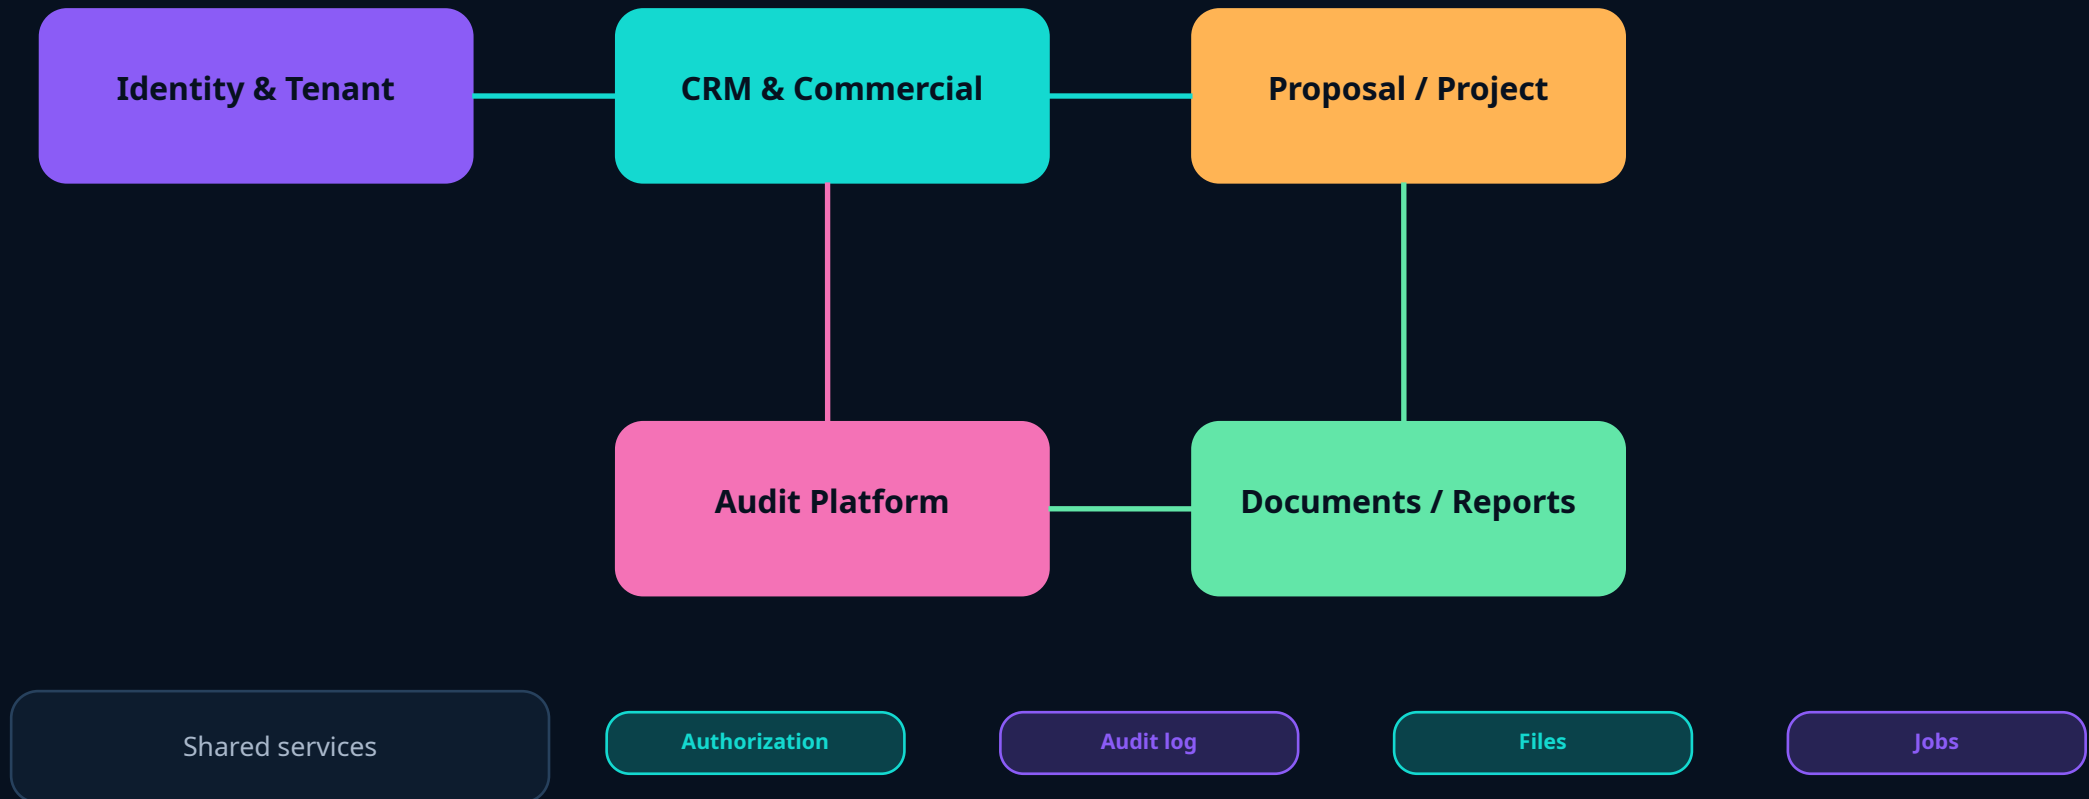

Design principle: modular monolith first, service extraction only when justified by scale or ownership

One journey from sale to certificate

The rebuild succeeds when the handoff between commercial and audit teams becomes predictable.



CRM / Sales

commercial trigger



Proposal

commercial trigger



Audit Date

commercial trigger



AR + Schedule

controlled delivery



Audit + TR

controlled delivery



Decision + Issuance

controlled delivery

Backend-driven stepper | active stage editable | completed stage read-only | every transition auditable

What we borrow from Gauzy and what stays uniquely OneAlpha

This boundary prevents the rebuild from becoming a generic ERP project.

REFERENCE AREA	DECISION	ONEALPHA TRANSLATION
Tenant / permission model	Adapt	Master Tenant, Keycloak, tenant-scoped policies
CRM / proposals / projects	Adapt	CBQA proposal, scope, methodology, audit-date rules
Generic HR / time / inventory	Defer	Add only when a clear OneAlpha business case exists
Audit workflow / certificate	Own	ISO, ISCC, LVV, LATIK, Transfer Audit rules
Plugins / MCP / integrations	Adapt	Read-only by default, allowlisted mutations

The largest risks are controllable, but only with gates


A phased rebuild reduces the blast radius and keeps business decisions visible.

Scope explosion	High	Freeze capability map; phase generic modules
License / code reuse	High	Legal gate before source/package reuse
Workflow regression	High	State machine + C1-C9 E2E baseline
Migration integrity	High	Dry-run, mapping table, reconciliation, rollback
Agent overreach	Med	Worktrees, contracts, approvals, protected paths
Infrastructure weight	Med	Start minimal; add Redis/search/analytics by need

Risk posture: make uncertainty explicit before implementation starts

Agents accelerate execution when the work is partitioned and reviewable


The harness coordinates specialist agents. Humans retain architectural, migration, and production authority.

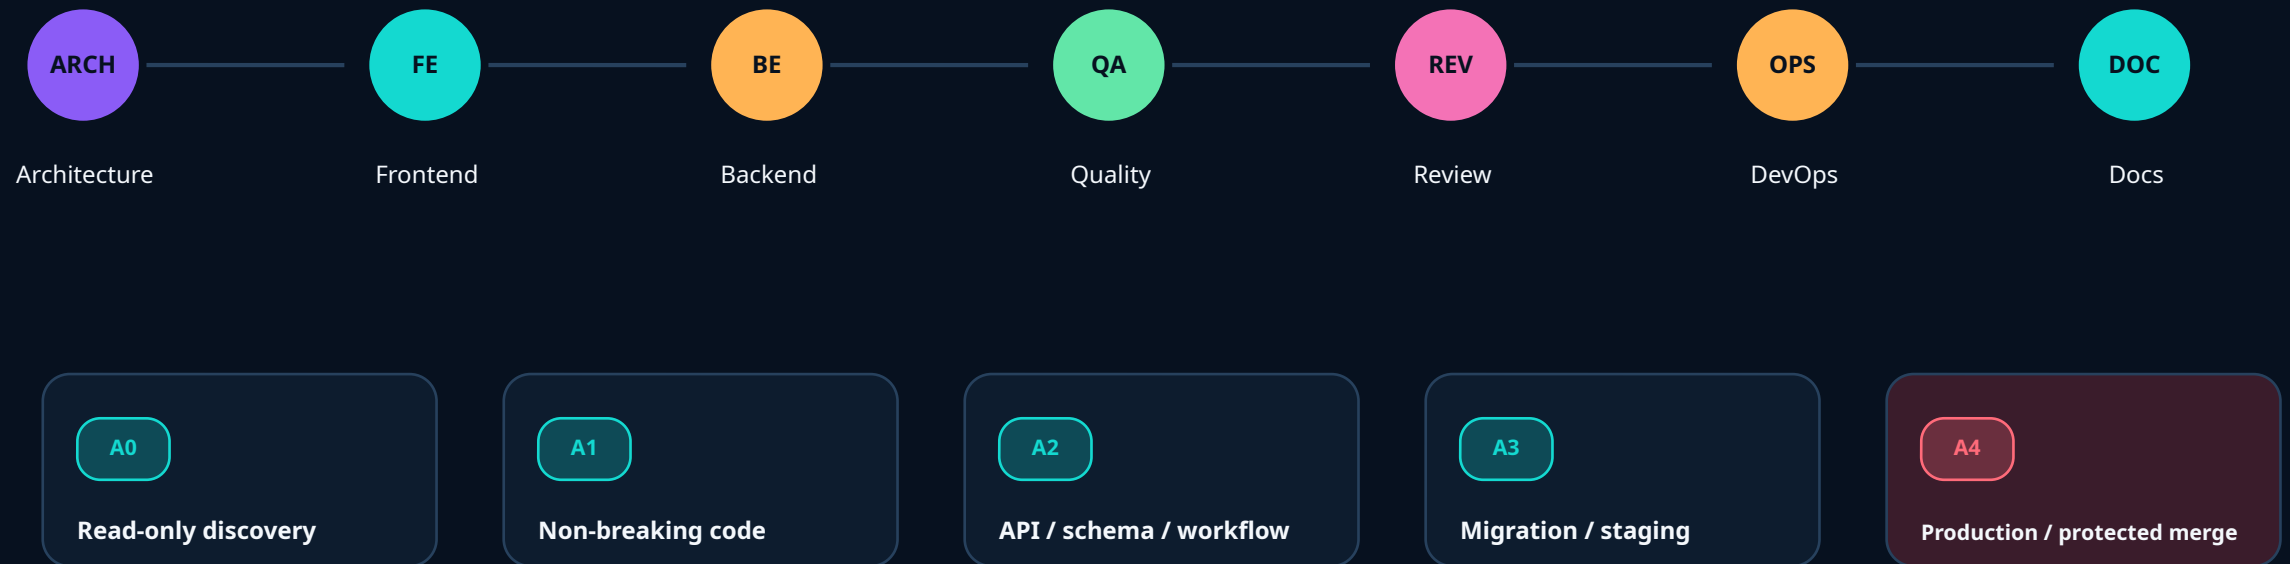

Every task returns changed files, tests, risks, evidence, and follow-up work

Sequence the rebuild around risk, not around a wish list

Each milestone produces something management can inspect and approve.

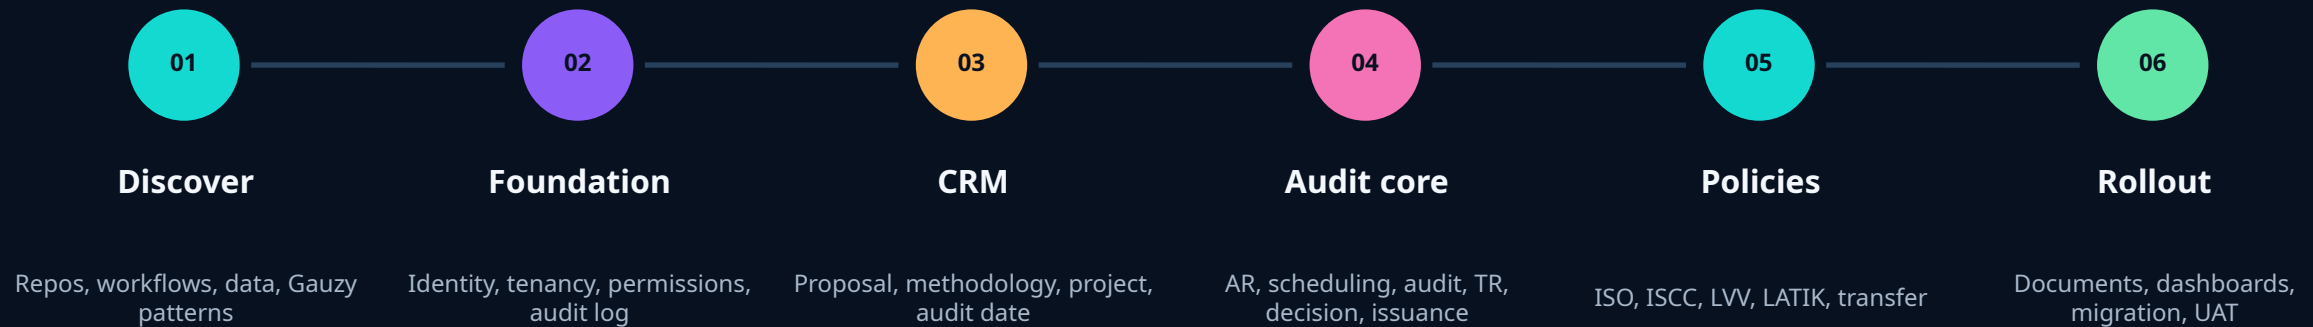

First approval requested: Discovery only. No migration, no deployment, no broad code rewrite.

Approve a controlled rebuild with three decision checkpoints

The proposal protects continuity while creating a stronger platform for future modules.



Approve discovery

Read-only inventory and adoption boundary



Approve foundation

Tenant, authorization, workflow contracts, test base



Approve pilot rollout

CRM-to-certificate flow with UAT evidence

Recommended decision: proceed with Path C, reference + rebuild, starting with ONEALPHA-DISCOVERY-001.

The ask

Approve the first gate

A read-only discovery sprint that turns Gauzy inspiration and OneAlpha reality into an approved build map.

Next artifact: discovery report + ADR adoption boundary

ONEALPHA

CRM. Audit. One operating core.
